

REQUEST FOR PROPOSALS CONSTRUCTION MANAGER AS CONSTRUCTOR

March 23, 2017

Addendum No. 1

1. A preliminary Project Budget which includes all anticipated work items is included for reference in preparing a response to this Request for Proposal.
2. A preliminary Project Schedule which includes all anticipated work item locations is included for reference in preparing a response to this Request for Proposal.

South Montgomery Community School Corporation
PO Box 8
New Market, IN 47965

March 23, 2017

Project Budget Summary

High School

Site/Circulation	\$	5,584,000
Safety/Security	\$	140,000
Building Envelope	\$	-
Building Interior Spaces	\$	4,526,300
Building Systems	\$	900,000
Construction Costs	\$	11,150,300
Soft Costs	\$	2,787,575
Total	\$	13,937,875

Walnut Elementary School

Site/Circulation	\$	324,000
Safety/Security	\$	102,066
Building Envelope	\$	993,396
Building Interior Spaces	\$	1,063,995
Building Systems	\$	1,313,369
Construction Costs	\$	3,796,826
Soft Costs	\$	949,206
Total	\$	4,746,032

Ladoga Elementary School

Site/Circulation	\$	380,000
Safety/Security	\$	520,956
Building Envelope	\$	673,692
Building Interior Spaces	\$	860,736
Building Systems	\$	1,292,306
Construction Costs	\$	3,727,690
Soft Costs	\$	931,923
Total	\$	4,659,613

New Market Elementary School

Site/Circulation	\$	243,500
Safety/Security	\$	313,154
Building Envelope	\$	1,369,809
Building Interior Spaces	\$	1,246,770
Building Systems	\$	2,082,440
Construction Costs	\$	5,255,673
Soft Costs	\$	1,313,918
Total	\$	6,569,592

Administrative Offices	\$	-
Soft Costs	\$	-

Total	\$	-
District-wide Needs	\$	-
Soft Costs	\$	-
Total	\$	-
Total Project Costs	\$	29,913,112

March 23, 2017

**Southmont JR/SR High School Additions and Renovations
217009.00**

High School
Project Budget Estimates

<u>Item</u>	<u>Total</u>
Site/Circulation	
Campus Master Plan	
PE/Athletics	
A Basebal complex	\$ 925,000
B Softball complex	\$ 625,000
C BB/SB Support Building	\$ 756,250
D Soccer complex	\$ 210,000
E Practice Football complex	\$ 180,000
F1 Stadium synthetic turf ¹	\$ -
F2 New Sports Lighting	\$ 225,000
G Stadium team building	\$ 1,375,000
Parking	
H Soccer parking	\$ 240,000
I Football parking	\$ 187,500
J BB/SB parking	\$ 123,750
Lighting Replacement	\$ 100,000
Additional Parking	
K 100 on east side	\$ 281,250
L 40 on east side	\$ 56,250
Reconfigure drive lanes	\$ 75,000
Drive	
New North Drive	\$ 224,000
Subtotal	\$ 5,584,000
Safety/Security	
Replace hardware as needed	\$ 70,000
Security at JH cafeteria corridor	\$ 30,000
New digital cameras	\$ 40,000
Subtotal	\$ 140,000
Building Interior Spaces	
Restrooms	
Remodeling (4 group restrooms)	\$ 60,000
Locker Rooms	
Renovation	\$ 1,110,000
Career and Technical Ed. Improvements	
Remodeling	\$ 795,000

FANNING HOWEY

New Construction	\$ 1,945,800
Woods Lab Improvements	\$ 80,500
Ag/Horticulture Improvements	
Lab/classrooms	\$ 280,000
Greenhouses	\$ 150,000
Culinary Arts Lab finishes remodeling	\$ 105,000
Subtotal	\$ 4,526,300
Building Systems	
JH and HS Gyms- Air Conditioning	\$ 900,000
Subtotal	\$ 900,000
Total Construction Costs	\$ 11,150,300
Soft Costs	25% \$ 2,787,575
Total	\$ 13,937,875

Notes:

1. Not included in this project

March 23, 2017

**Walnut Elementary School Additions and Renovations
2170011.00**

Project Budget Estimates

<u>Item</u>	<u>Total</u>
Site/Circulation	
New sewage treatment plant	\$ 250,000
Playground equip. improvements	\$ 50,000
Lighting Replacement	\$ 24,000
Subtotal	\$ 324,000
 Safety/Security	
New digital camera system	\$ 102,066
Subtotal	\$ 102,066
 Building Envelope	
Reroof entire building	\$ 612,396
Replace exterior windows/doors	\$ 153,000
Provide new entry vestibule	\$ 228,000
Subtotal	\$ 993,396
 Building Interior Spaces	
Remodel office	\$ 180,000
Repurpose music room	\$ 58,500
Remodel finishes	\$ 765,495
Install new marker boards	\$ 20,000
Renovate north group restrooms	\$ 40,000
Subtotal	\$ 1,063,995
 Building Systems	
HVAC systems replacement	\$ 1,224,792
Replace PA system	\$ 41,626
Add phones in all rooms	\$ 46,950
Subtotal	\$ 1,313,369
 Total Construction Costs	 \$ 3,796,826
Soft Costs	25% \$ 949,206
Total	\$ 4,746,032

March 23, 2017

**Ladoga Elementary School Additions and Renovations
217010.00**

Project Budget Estimates

<u>Item</u>	<u>Total</u>
Site/Circulation	
Taylor Street improvements	\$ 200,000
Drainage improvements	\$ 75,000
Playground equip. improvements	\$ 50,000
Increase west sidewalk width	\$ 25,000
Lighting Replacement	\$ 30,000
Subtotal	\$ 380,000
Safety/Security	
New secure main entrance/admin.	\$ 435,000
New digital camera system	\$ 85,956
Subtotal	\$ 520,956
Building Envelope	
Reroof entire building	\$ 601,692
Replace exterior windows/doors	\$ 72,000
Subtotal	\$ 673,692
Building Interior Spaces	
Repurpose existing office area	\$ 90,000
Improve classroom acoustics	\$ 20,000
Repurpose music room	\$ 20,000
Remodel finishes	\$ 515,736
Install new marker boards	\$ 20,000
Remodel group restrooms	\$ 60,000
Selective kitchen equip. replacement	\$ 75,000
Gym railings/curtain replacement	\$ 60,000
Subtotal	\$ 860,736
Building Systems	
HVAC systems replacement	\$ 1,031,472
Provide new sprinkler system	\$ 171,912
Replace PA system	\$ 34,382
Add phones in all rooms	\$ 39,540
Improve wireless coverage	\$ 15,000
Subtotal	\$ 1,292,306
Total Construction Costs	\$ 3,727,690
Soft Costs	25% \$ 931,923
Total	\$ 4,659,613

FANNING HOWEY

March 23, 2017

New Market Elementary School Additions and Renovations 217012.00

Project Budget Estimates

<u>Item</u>	<u>Total</u>
Site/Circulation	
New bus drop-off/pick-up lot	\$ 112,500
Repurpose existing drop-off pick-up lot	\$ 20,000
Playground equip. improvements	\$ 50,000
Provide additional walks at playgrounds	\$ 25,000
Lighting Replacement	\$ 36,000
Subtotal	\$ 243,500
Safety/Security	
Expand secure vestibule and office entrance	\$ 152,000
New digital camera system	\$ 161,154
Subtotal	\$ 313,154
Building Envelope	
Reroof entire building	\$ 1,208,655
Resolve soffit/venting issues	\$ 161,154
Subtotal	\$ 1,369,809
Building Interior Spaces	
Add group restrooms	
Cafeteria	\$ 135,000
North Wing	\$ 180,000
Update staff lounge	\$ 20,000
Replace gym bleachers	\$ 75,000
Remodel finishes	\$ 805,770
Install new marker boards	\$ 20,000
Add stepped story areas in 2 Kindergarten rooms	\$ 11,000
Subtotal	\$ 1,246,770
Building Systems	
HVAC systems replacement	\$ 1,933,848
Replace PA system	\$ 64,462
Add phones in all rooms	\$ 74,131
Replace gym sound system	\$ 10,000
Subtotal	\$ 2,082,440
Total	\$ 5,255,673
Soft Costs	25% \$ 1,313,918
Total	\$ 6,569,592

March 23, 2017

New Administrative Offices
217013.00

Project Budget Estimates

	<u>Total</u>
New facility/offices/board room/storage ²	\$ -
Site for 50 vehicle parking ¹	\$ -
<hr/>	
Total	\$ -

Notes:

1. Bulk of cost in HS Project Campus Site Improvements
2. Not included in this Project

March 23, 2017

Wide Area Network
217016.00


Project Budget Estimates

Total

Fiber Optic Connections to all Campuses¹

Notes:

1. Not included in this project

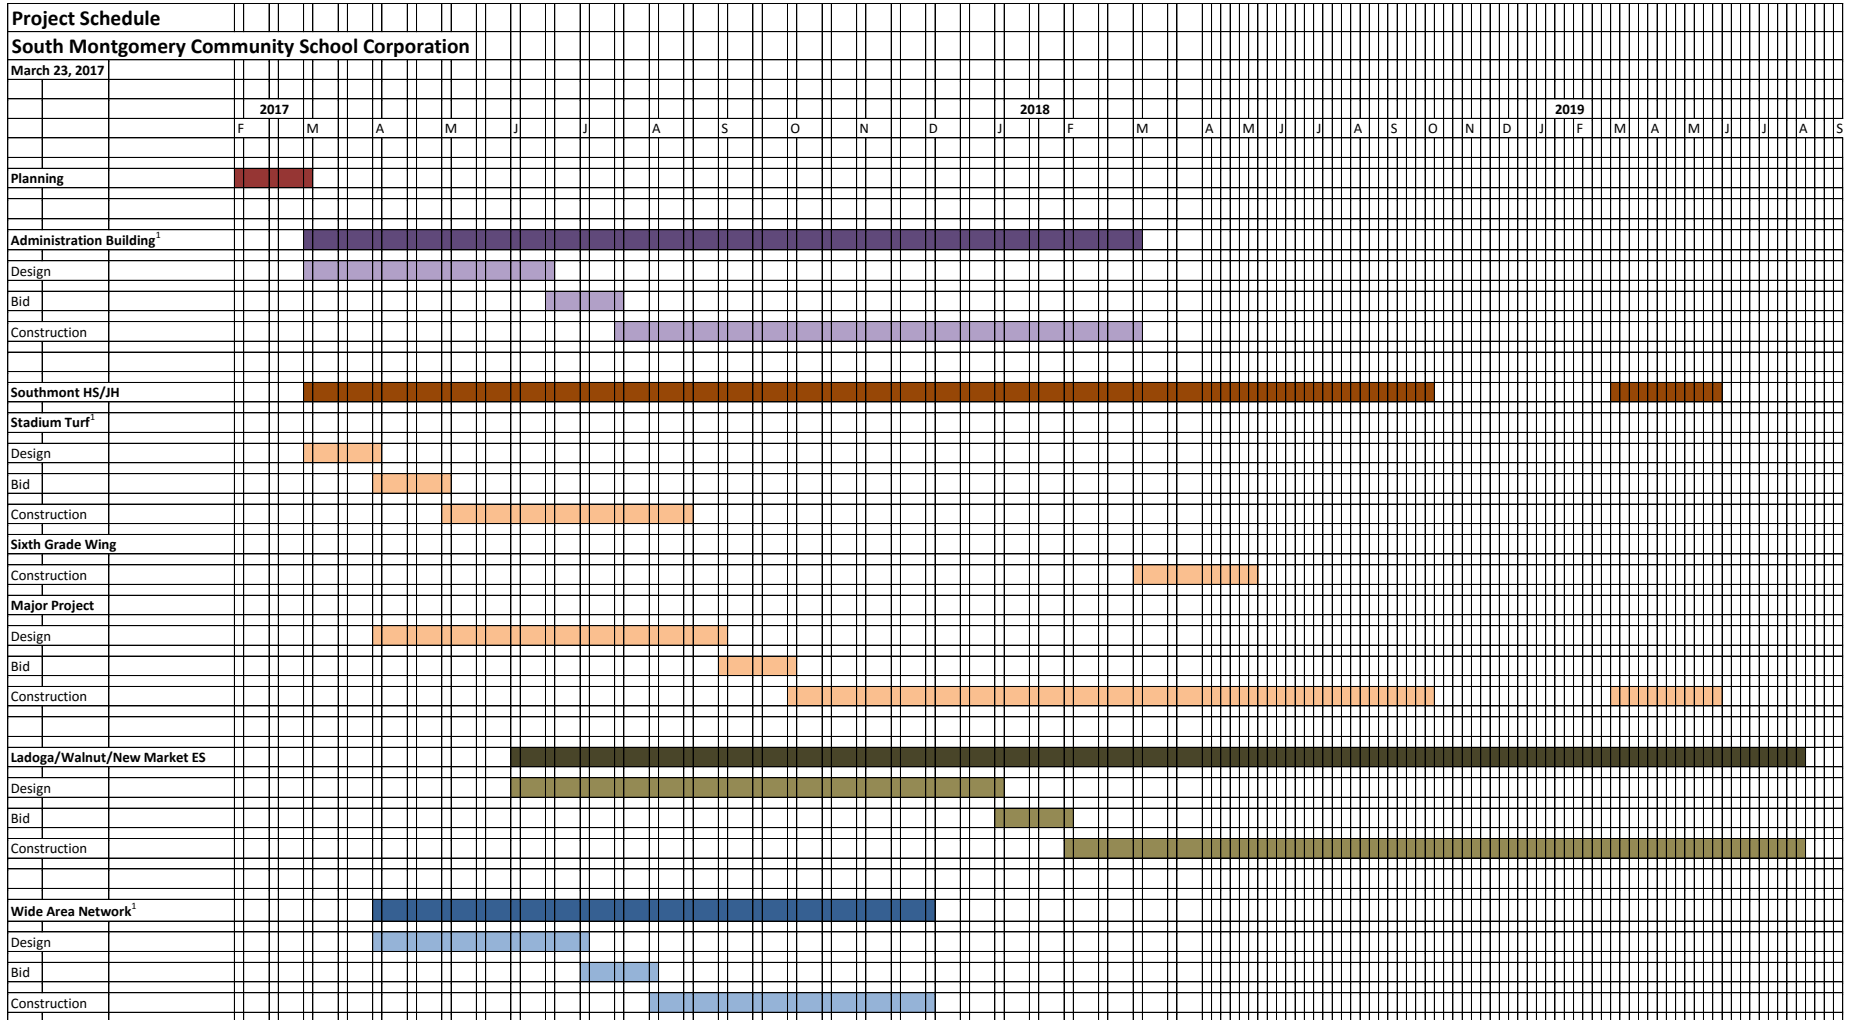

Notes:
 1. Work not included in CMc contract
